

# Saline Waste Water Treatment Plant Equipment Status Report



Form Revised 09 / 20 / 2021

Equipment/Process/Resource	Status	Timeline
Influent and Grit Removal	Yellow	Two to thirty-six months
Comments: Yellow - Install automatic bar screen rake to reduce influent backup and surge (Phase I) Yellow - Replace influent pumps (Phase I) Green - Repaired bearing on grit mechanism (July 2021); replaced grit pump (September 2021)		
Primary Clarifiers	Yellow	Three to six months; ongoing
Comments: Green - Regular maintenance and cleaning; target cleaning of internal components in fall 2021 Green - Repaired arm mechanism (August 2021) Yellow - Sludge pump packing replaced; planned rebuild of pump (target fall 2021)		
RBCs	Green	Ongoing
Comments: Green - Regular maintenance and cleaning; reviewing new practices for monitoring bio-health		
Secondary Clarifiers	Yellow	One to six months
Comments: Yellow - Secondary sludge and scum line cleaning completed winter 2021; secondary sludge pump installed and operating. In process of working through accumulated sludge. Yellow - Considering covers for secondary clarifiers as part of future plant improvement phase		

## Status Key

**Red:** Not operating to design standards; **Yellow:** Operating but not to optimal standards; **Green:** Operating as designed  
significant improvements/repairs needed issue has been identified and/or plan in place

# Saline Waste Water Treatment Plant Equipment Status Report



Equipment/Process/Resource	Status	Timeline
Digestors	Yellow	One to twenty-four months
Comments: Yellow - Electrical repairs completed on flare (March 2021), repairs pending on dehumidifier/chiller Green - Cleaning of interior lining completed (September 2021). Green - Over flow line and valves replaced as part of sludge pump program (June/July 2021) Yellow - Replace existing cover (Phase I)		
Sludge Holding	Green	Ongoing
Comments: Green - Regular maintenance and cleaning; sludge hauling performed late July 2021, next scheduled Oct. Green - Implemented new procedures to keep tanks sealed on a more frequent basis.		
Bioscrubbers and Odor Control	Yellow	Two to four months
Comments: Yellow - Weatherization project for bioscrubber; replaced non-potable water pumps (June 2021) Green - Re-acclimated organisms and maintaining appropriate pH. (Completed April 2021) Green - Boiler/heat exchange repaired and air handler functioning. (Completed March 2021)		
Tertiary Filters and UV	Yellow	Ongoing
Comments: Yellow - Maintenance contract executed August 2021, next maintenance late fall 2021/ winter 2022 Green - All mechanical elements functioning as designed		

## Status Key

**Red:** Not operating to design standards; **Yellow:** Operating but not to optimal standards; **Green:** Operating as designed  
significant improvements/repairs needed issue has been identified and/or plan in place


# Saline Waste Water Treatment Plant Equipment Status Report



Equipment/Process/Resource	Status	Timeline
Human Behavior	Yellow	Three to six month
Comments: <p>Yellow - Launch a public awareness campaign to improve education on how to reduce strain on existing systems</p> <p>Green - Created citizen odor complaint survey to track time, location, conditions of peak odor</p>		
Effluent	Yellow	Ongoing
Comments: <p>Yellow - Currently monitoring NPDES limits for ammonia</p> <p>Green - Installed additional chemical feed point for phosphorus removal</p>		
Additional Comments: <p>The City WWTP does not receive outside septic.</p>		

## Status Key

**Red:** Not operating to design standards; significant improvements/repairs needed  
**Yellow:** Operating but not to optimal standards; issue has been identified and/or plan in place  
**Green:** Operating as designed

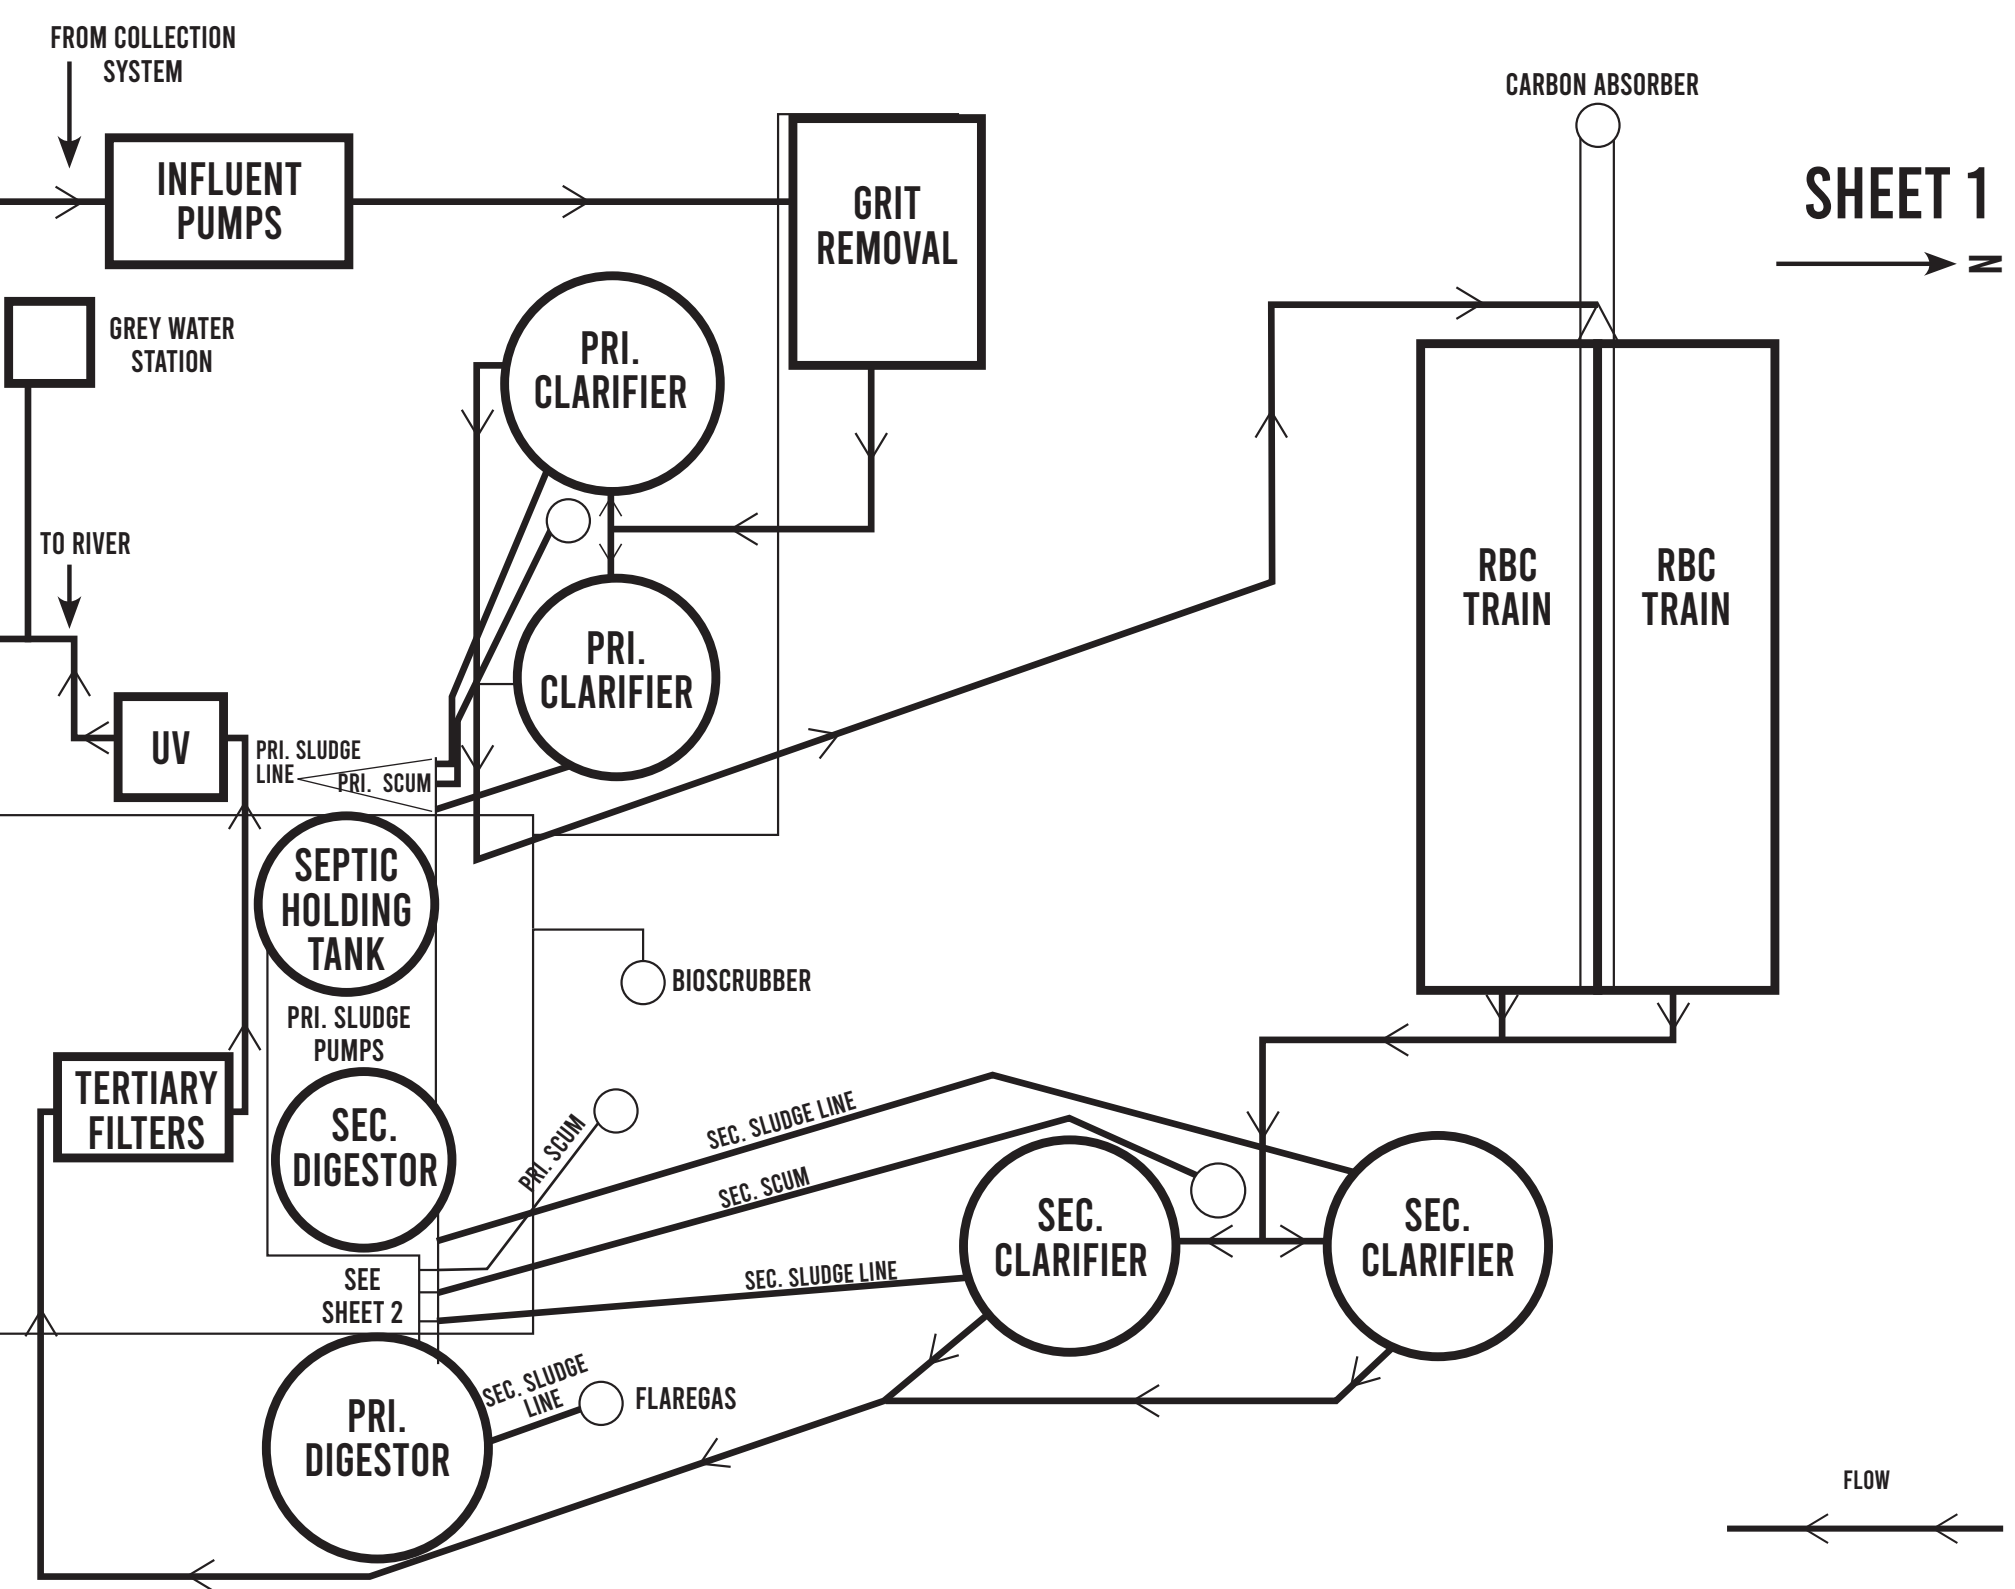

# SHEET 2

*\*BIRDS EYE VIEW*



WALL

SEC.  
SLUDGE

PRI.  
SCUM

SEC.  
SCUM

SEC.  
SLUDGE

TO  
FLOOR  
DRAIN

UP

TO OVERFLOW LINE

SEE  
SHEET 3


PRIMARY  
DIGESTOR


SECONDARY  
DIGESTOR


TO  
PRI SLUDGE  
PUMPS

FLOW CAN GO EITHER  
WAY ON THEIS LINE  
DEPENDING ON VALVES

✕ VALVE

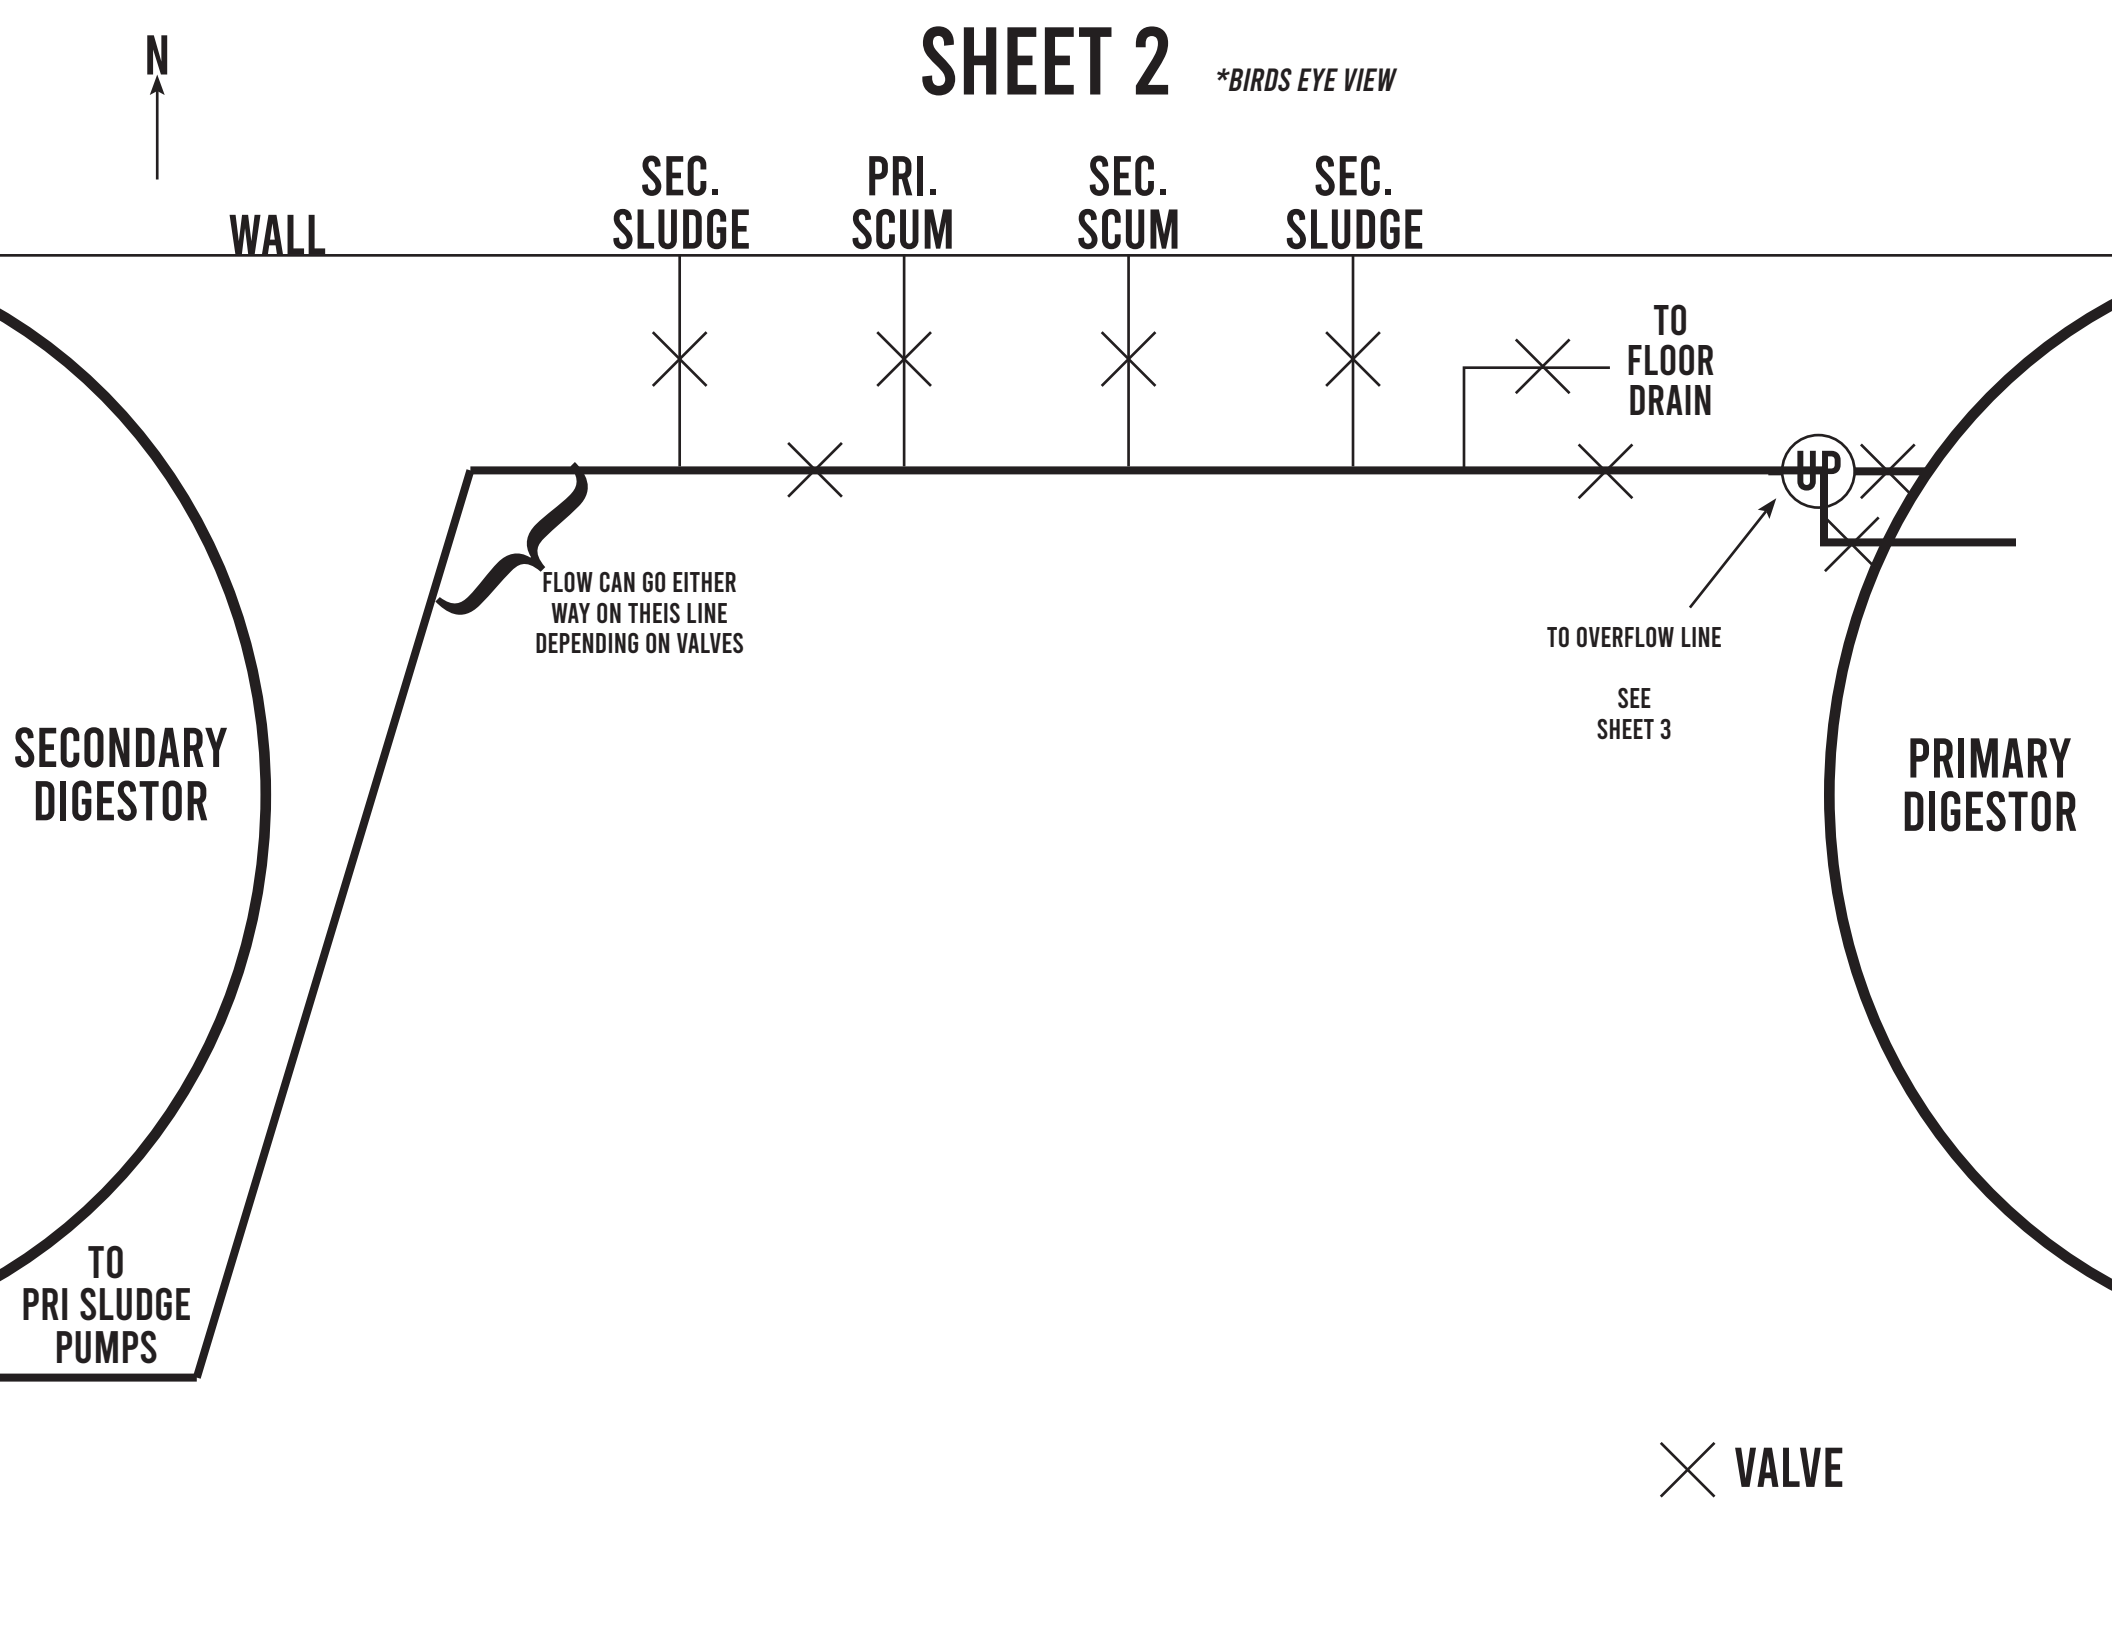

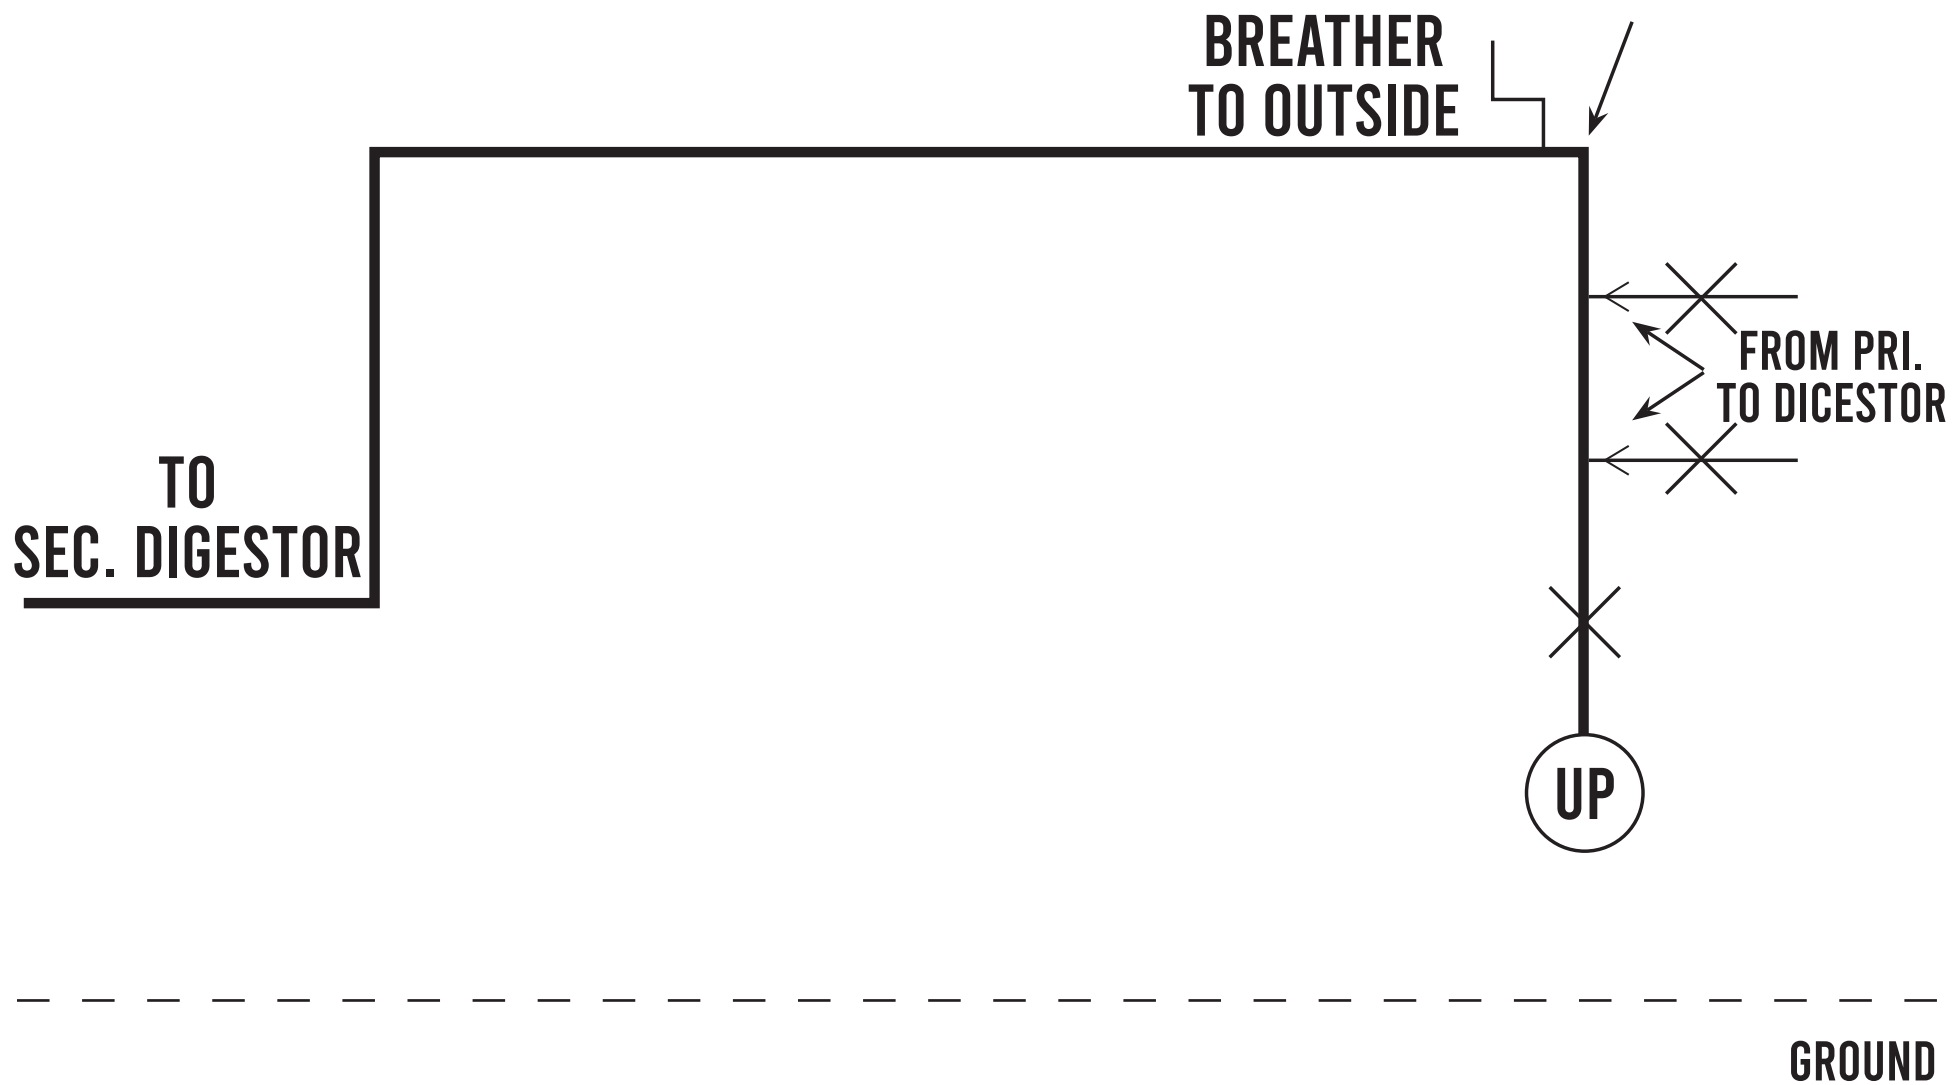

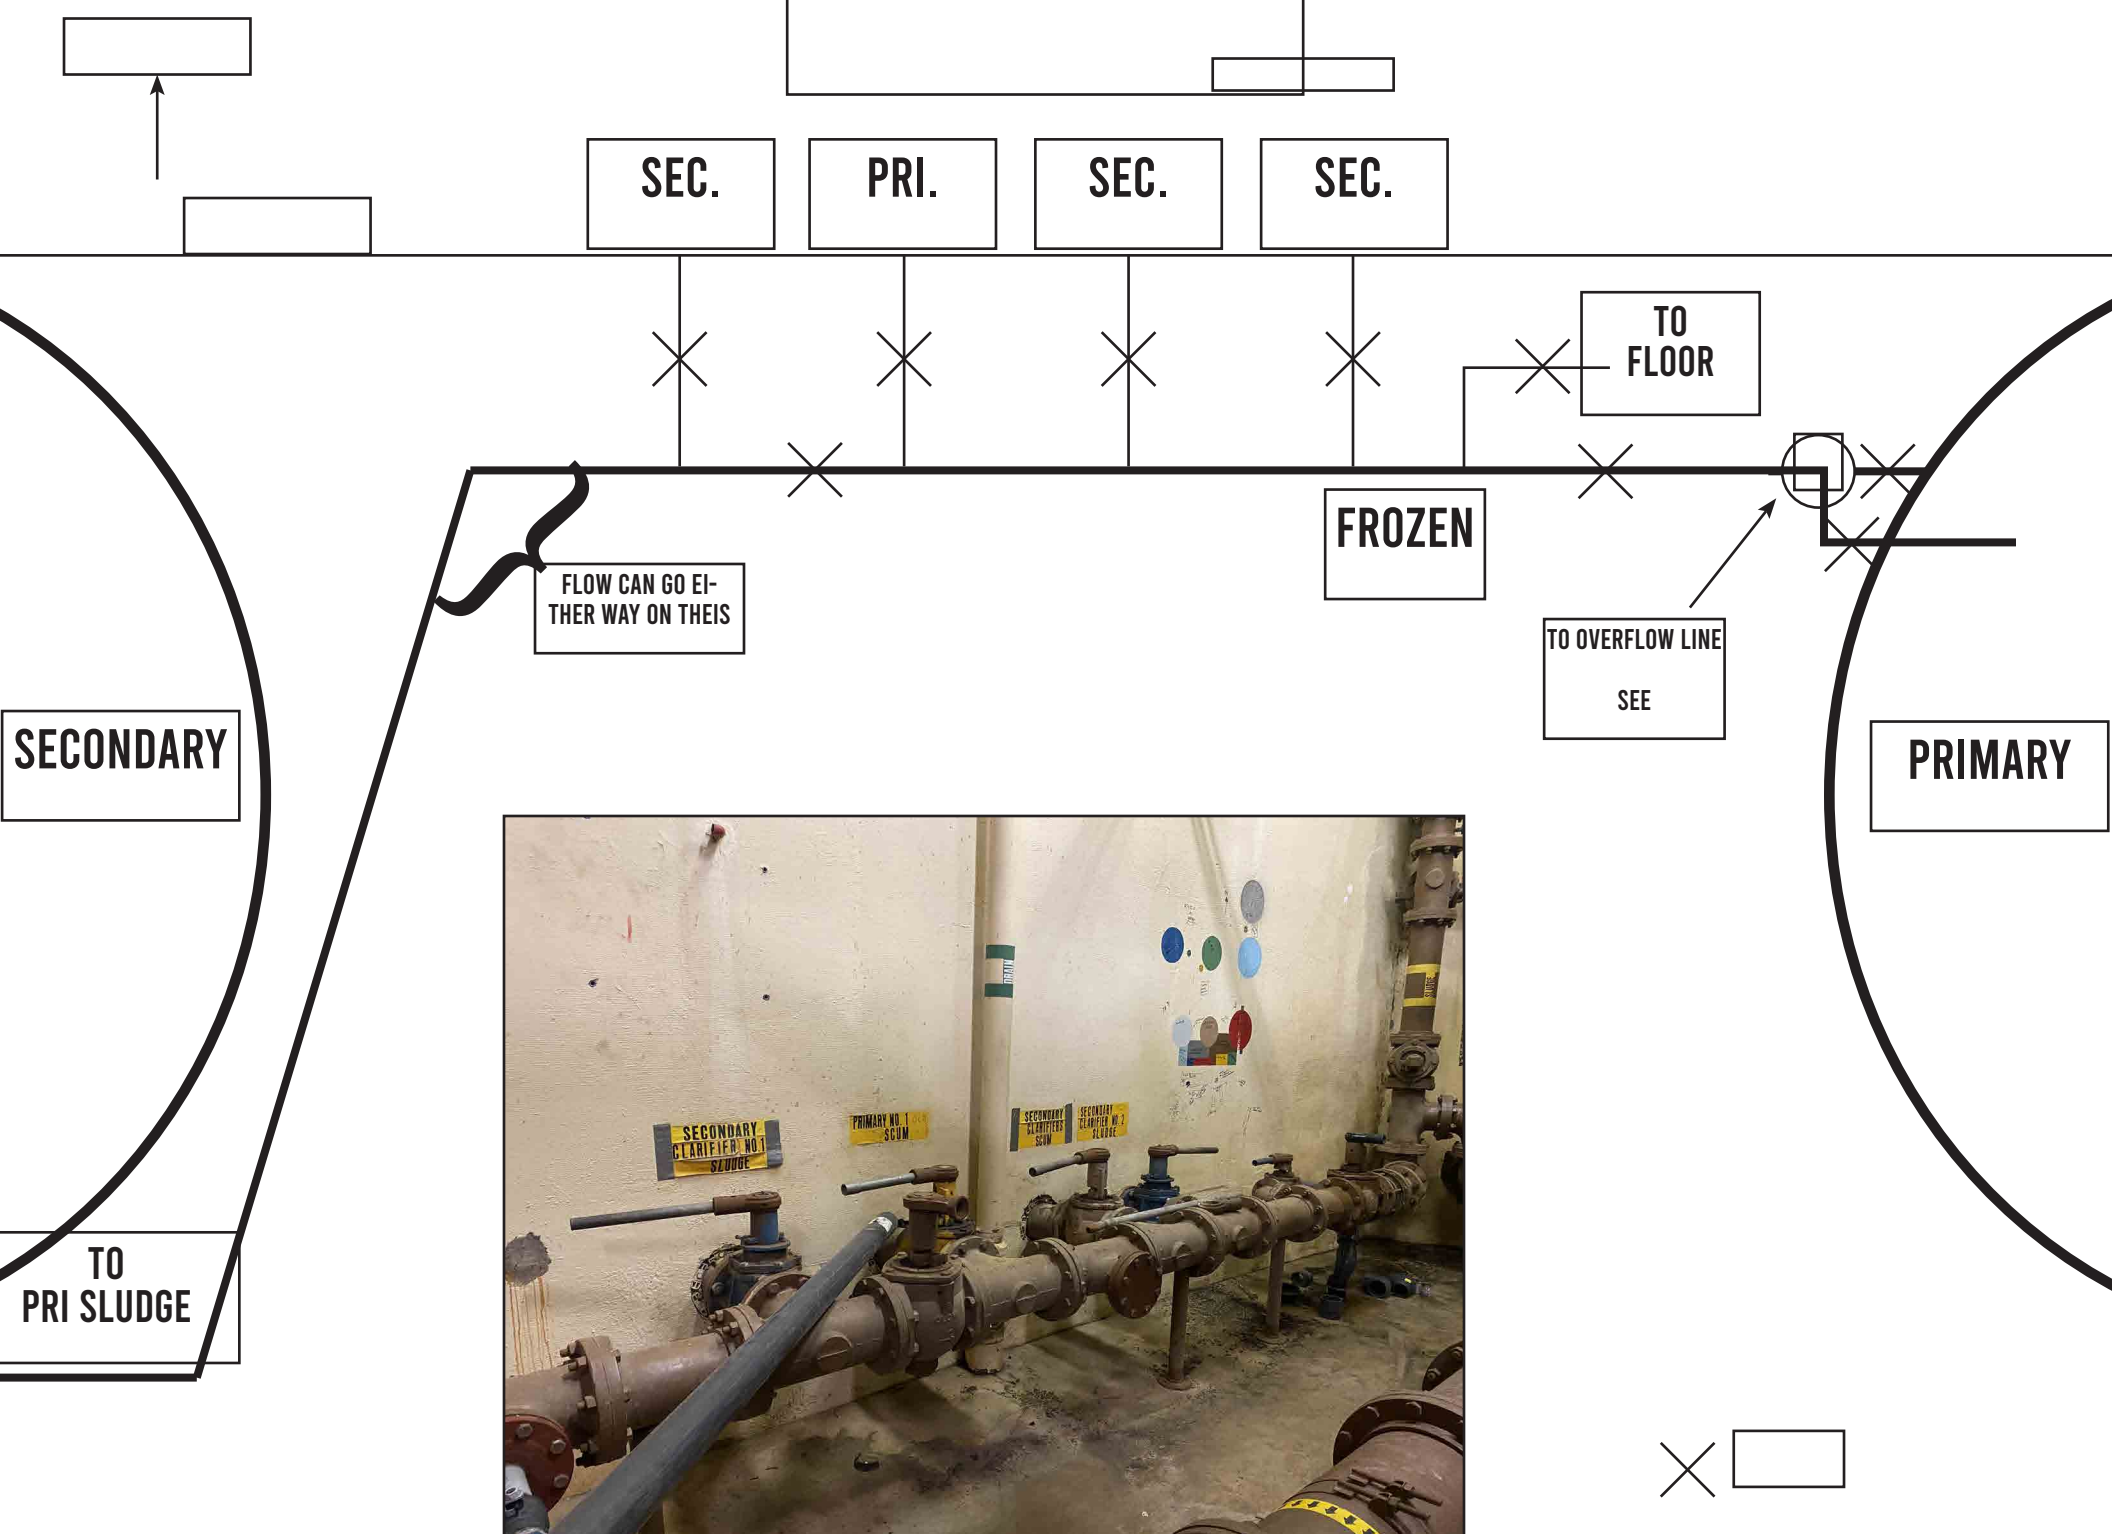



**BREATHER  
TO OUTSIDE**

**TO  
SEC. DIGESTOR**

